DEPI GRADUATION PROJECT · ODOO CONSULTANT TRACK

Smart Core.

Odoo 19 Enterprise implementation for Beitak Smart

Home appliances: import, distribution, showroom retail and in-house assembly.

PRESENTED BY KHOMASI ERP

AF **Ahmed Fahmy**
Project Manager & Manufacturing

LZ **Lobna Zanaty**
Accounting

MS **Mayada Salah**
Inventory

NG **Noha Gamal**
Sales, CRM & POS

OF **Omar ElSayed**
HR, Purchase & Technical

Go-live · 1 January 2027

IMPORT · ASSEMBLY · SHOWROOM · ACCOUNTING

AGENDA · 6 PARTS

What we will cover

01

The client

Who Beitak Smart is and how it works today

02

The problem

14 pain points costing money and visibility

03

Our approach

Methodology, documents and governance

04

The solution

9 modules, 70 requirements, 11 customizations

05

The data

Entity data and 27 import files

06

Delivery

UAT, training, go-live and investment

PART 01 / 05

The client

01

Beitak Smart — an appliance business running on a legacy accounting package, Excel and a standalone cashier program.

Beitak Smart

Snapshot · Today

SECTION · DIVIDER

CLIENT SNAPSHOT

Beitak Smart at a glance

Imports and distributes appliances, assembles its own fan and components, and sells through a Cairo showroom.

CAIRO · EGYPT

EST. APPLIANCE HOUSE

40	20	5	36	30
APPLIANCE MODELS	BRANDS	WAREHOUSES	EMPLOYEES	ODOO USERS

01

Trading

Imports from China in USD and buys from local agents; sells to 12 retailers, 2 distributors and 3 corporate clients.

02

Assembly

Own-brand stand fan, control boards, metal casings, harnesses and filters in A Cairo assembly unit.

03

Retail

Cairo showroom selling to walk-in customers on a standalone cashier program.

04

Services

Air-conditioner and TV wall-mount installation sold with the appliance.

DISCOVERY · 14 PAIN POINTS

The problems we found

14 pain points from discovery workshops with every department — the six with the highest impact.

TOP 6 OF 14
HIGHEST IMPACT

PP-01

Landed costs never reach item cost

Freight, duties and clearance stay in Excel, so margins look better than they are.

MARGIN · COSTING — High

PP-03

Stock-outs and overstock

No min / max rules against 45-60 day import lead times.

INVENTORY · SERVICE — High

PP-05

Assembled product cost unknown

Component consumption, labour and scrap are never recorded.

MFG · COSTING — High

PP-07

Receivables out of control

Cheques tracked in Excel; credit limits exist on paper only.

FINANCE · TREASURY — High

PP-09

No profitability by line or branch

Management cannot tell trading from manufacturing, Or Cairo from Asyut.

REPORTING · MGMT — High

PP-10

Month-end close takes 15 days

Everything is re-keyed between Excel and the legacy package.

ACCOUNTING · CLOSE — High

OUTCOMES · 8 KPIS

What success looks like

Eight KPIs agreed with the client, measured six months after go-live.

HORIZON
T + 6 MONTHS



Baselines are discovery estimates. Scale: 0 → 120.

Also measured

4 SECONDARY KPIS

- ✓ Landed costs allocated on **100%** of import shipments
- ✓ P&L by branch and business line available by working day **5**
- ✓ **100%** of B2B opportunities tracked in the CRM pipeline
- ✓ Showroom sales posted to stock and accounting daily instead of weekly

TOTAL KPIS **8**

PART 02 / 05

How we ran the project

02

Eight phases, seven milestones, and a document at every gate.

8 phases | 7 milestones | Document at every gate

SECTION · DIVIDER

METHODOLOGY · 13 WEEKS

Implementation methodology

13 weeks from kick-off on 4 October 2026 to go-live on 1 January 2027, then four weeks of hypercare.

PHASES · MILESTONES
8 + 6

P1	P2	P3	P4	P5	P6	P7	P8
Discovery	Analysis	Design	Build & migrate	UAT	Training	Cutover	Hypercare
W1-2	W2-4	W4-5	W6-9	W10-11	W11-12	W13	Jan

MILESTONES WITH CLIENT SIGN-OFF

6 gates · M2 → M7

M 2	M 3	M 4	M 5	M 6	M 7
22 Oct 2026	5 Nov 2026	3 Dec 2026	17 Dec 2026	1 Jan 2027	28 Jan 2027
BRD signed	Design & proposals signed	Build & migration complete	UAT signed	Go-live	Hypercare closed

REPOSITORY · ONE GITHUB REPO

What we delivered

Four folders in one GitHub repository — every document traceable to the one before it.

GITHUB.COM / KHOMASI / SMART-CORE

01

Presentation

- Slide deck (PPTX + PDF)
- Demo video of the live system

2 ITEMS / DECK

02

Preparations

- Company Profile
- Project Name & Scope
- Team & Roles + RACI
- Basic Database Configuration

4 ITEMS / PREP

03

Project documents

- BRD · RTM · GAWF · SSD
- TPD · FPD + cost model
- UPD · TD · UDP · UATD

3 GROUPS / DOCS

04

Entity data & setup

- 3 entity-data workbooks
- 27 Odoo import files
- Go-Live & Deployment Plan

3 STREAMS / DATA

PART 03 / 05

The solution

03

Nine Odoo modules covering every department, designed around 70 agreed requirements.

9 modules | ✓ 70 requirements | 1 database

SECTION · DIVIDER

THE BUILD · 9 MODULES

Nine modules, one database

Each module owned by one consultant and signed off by one key user at the client.

ODOO 19 ENTERPRISE · 1 DB

AF

CRM

Pipeline for 6 sales teams, activities, lost reasons

01

NG

Sales

4 price lists, credit control, discount approval, margins

02

NG

Point of Sale

Cairo showroom: barcode, serials, cash / card / account

03

OE

Purchase

USD vendors, PO approval, three-way match, landed costs

04

MS

Inventory

5 warehouses, multi-step routes, 1,546 serials, counts

05

AF

Manufacturing

11 BOMs, 5 work centers, work orders, real cost

06

LZ

Accounting

Egypt localization, VAT & WHT, 9 journals, analytic P&L

07

OE

Employees

36 employees, time off, attendance kiosk


08

OE

Approvals

Purchase, payment, discount and credit-limit gates

09

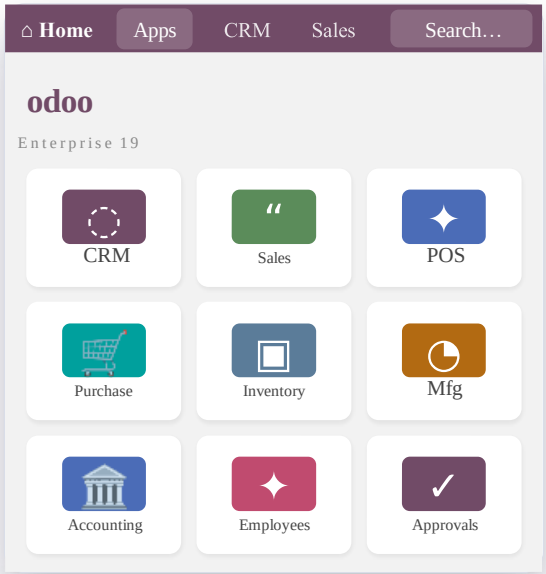

GAP ANALYSIS · 70 REQUIREMENTS

Standard first, customize last

70 requirements classified in the gap analysis — the programme guideline is roughly 70 / 10-15 / 15-20.



51	Standard Odoo	73%
8	Workaround	11%
11	Customization	16%

Why it matters

- ✓ **73% standard** keeps upgrades cheap and safe
- ✓ **11% workarounds** use standard features in a defined way, documented for training
- ✓ **16% customizations** are Studio fields, approval rules and report layouts — no custom modules

11 customizations

= 15 CONSULTANT DAYS

Bilingual invoice and delivery note, import container tracking, warranty dates, credit-limit and discount approval, commission and shipment cost reports.

Fixing the cost problem: procure to pay

From a USD purchase order in China to a product cost that finally includes freight, duties, clearance and insurance.

USD → EGP · LANDED COST

01 **RFQ & PO** — USD vendor price, GM approves

02 **Shipment** — Container, B/L, ETA on PO

03 **Receipt** — Input → QC → Stock, serials scanned

04 **Bills** — Freight, duties, clearance, insurance

05 **Landed cost** — Allocated to receipt lines

06 **Real cost** — Product cost and margin correct

BEFORE


Cost = invoice price only; freight and duties sat in Excel.

AFTER

Cost includes about 10% landed costs, so margin and COGS are real.

THE ACCOUNTING BEHIND IT

Receipt	Dr Inventory 1201xx Cr GRNI 120900
Vendor bill	Dr GRNI + VAT input Cr Payables 211200 (USD)
Cost bills	Dr Clearing 1301xx Cr Payables 211100
Landed cost	Dr Inventory 1201xx Cr Clearing 1301xx → zero

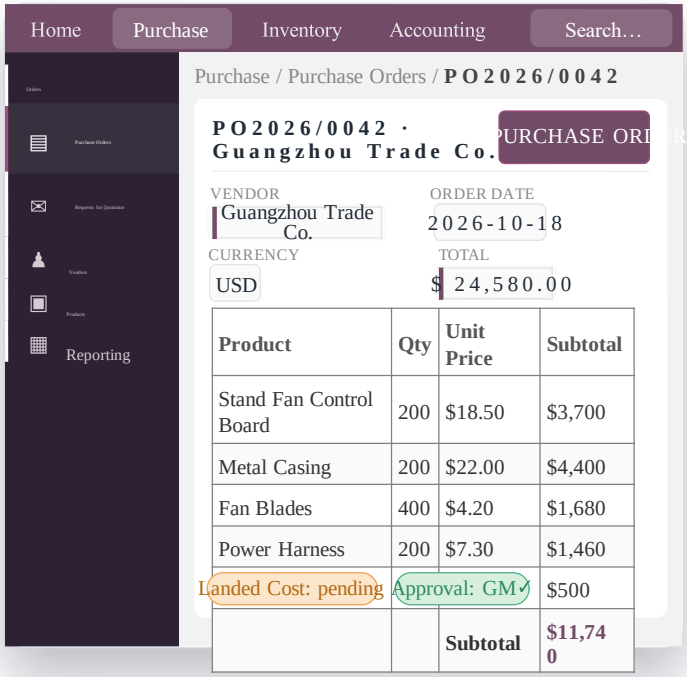


MANUFACTURING · MULTI-LEVEL BOM

Costing the Beitak stand fan

A multi-level BOM: the fan control board is produced first, then consumed by the fan — labour comes from work-center rates.

How the cost is built

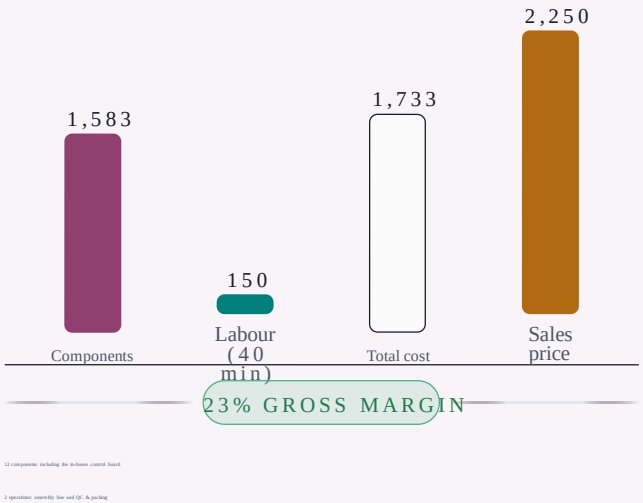

12 components including the in-house control board

2 operations: assembly line and QC & packing

AVCO valuation posts every move automatically


BOM: Stand Fan SF-18

BOM/0010

▼Stand Fan SF-18	1 unit	EGP 1,733
✓ Control Board (in-house)	1	EGP 412
✓ Metal Casing	1	EGP 280
✓ Fan Blades + Motor	1 set	EGP 540
✓ Harness + Filter + Misc	1 set	EGP 351

OPERATIONS

◔ Assembly Line	30 min	EGP 90
✓ QC & Packing	10 min	EGP 60

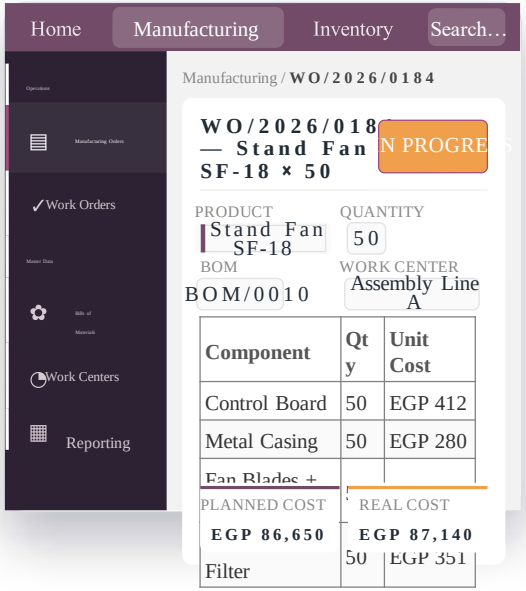

Before: the fan cost was a guess. Now every manufacturing order shows planned versus real cost.

11 BOMS COSTED

Selling with control

Pricing, credit and the showroom brought into the same system as stock and accounting.

Pricing
4 price lists (retail, wholesale, distributor, key account) with quantity breaks, all driven from the list price — one change updates every segment.

Credit control
Credit limit per customer with a warning on the order, and confirmation blocked above the limit until the Finance Manager approves.


Discounts
Any line discount above 10% needs Sales Manager approval, logged in the document chatter.

Showroom
POS linked to Cairo stock: barcode scanning, a serial captured for every appliance, cash / card / customer account, and a cash count at closing.

Traceability
1,546 serial numbers from receipt through delivery to warranty and returns.

Why the client cares: *Prices stop drifting between reps, overdue customers stop receiving goods, and showroom sales hit stock and the general ledger the same day instead of once a week.*

4 PRICE LISTS · 1,546 SERIALS

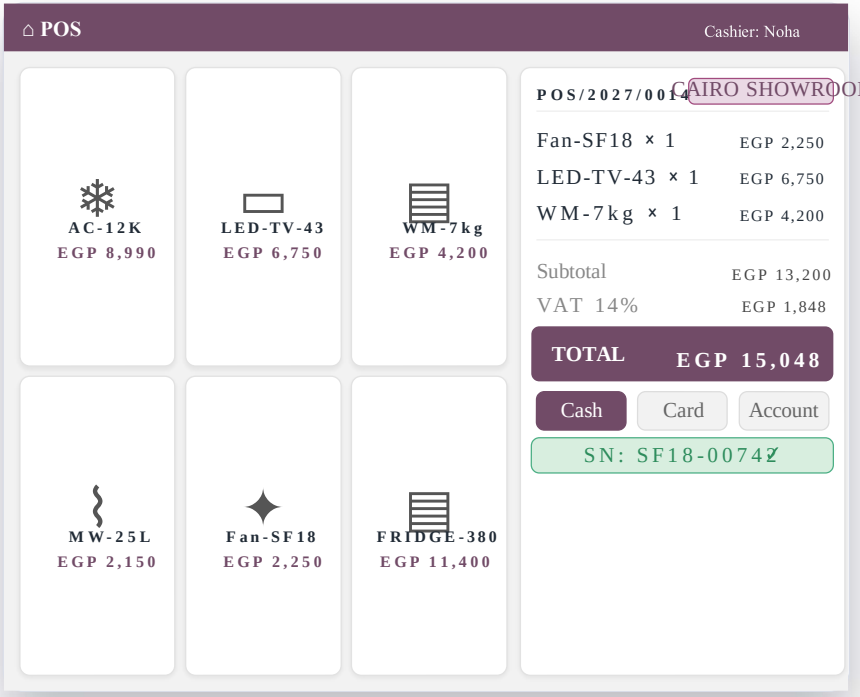

FINANCE · EGYPT LOCALIZATION

Accounting that closes in five days

Egyptian localization, two analytic plans, and every stock and sales movement posting itself.

CLOSE BY WD 5

61
ACCOUNTS ADDED
on top of the Egypt localization

9
JOURNALS
4 bank · 4 cash · opening

2
ANALYTIC PLANS
business line · branch

14%
VAT + WHT
1% / 2% / 3% withholding

Correct by design

COGS accounts are Cost of Revenue, inventory is valued per category, and interim accounts clear themselves.

Multi-currency


Only the CIB account is fixed in USD, so overseas bills post and the exchange difference lands in the right account.

Post-dated cheques

Received and issued cheques sit in notes accounts with their maturity date until they clear.

Profitability

P&L by trading, manufacturing and services, and by each of the five branches plus the showroom.

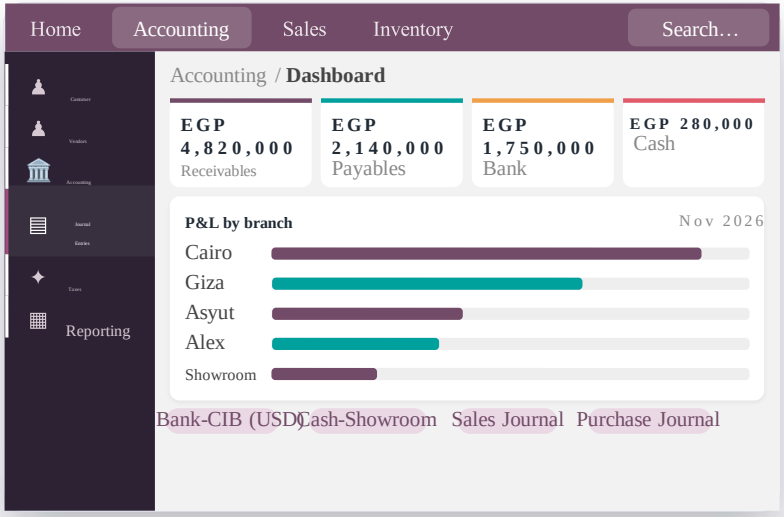

PART 04 / 05

The data behind the system

04

All 15 entity-data items collected, cleansed and turned into 27 ready-to-load import files.

Entity data | ✓ Opening balances | Segregation matrix

SECTION · DIVIDER

MIGRATION · 27 IMPORT FILES

Entity data and migration

Every figure in the deck comes from these files — they are the system, not a description of it.

89	11	32	1,546	36	27
PRODUCTS	BOMS	CUSTOMERS & VENDOR	SERIAL NUMBERS	EMPLOYEES	IMPORT FILES

Three entity-data workbooks

▣ .XLSX

01 **Organization & accounting**
org chart, users, chart of accounts, opening balances, banks, safes, journals, taxes

02 **Products & inventory**
categories, products, BOMs, work centers, price lists, warehouses, stock by location

03 **Partners & cycles**
customers, vendors, approvals matrix and six business cycles

Opening balances validated

✓ SIGNED OFF

Trial balance each side	40,474,776.50 EGP	BALANCED
Inventory = quantity × cost	20,424,776.50 EGP	REVIEWED
Receivables / payables split by partner, matched to aging	—	BALANCED
Clearing account 190100 zero after the opening entry	0.00	BALANCED

SECURITY · 30 USERS · 19 ACCESS PROFILES

Who can do what

30 users in 19 access profiles, with the requester and the approver never being the same person.

PROCESS	REQUESTER	APPROVER	THRESHOLD
Purchase	Buyer creates the order	Procurement Manager approves above	250,000 EGP
Payment	Treasurer prepares the payment	Finance Manager posts above	500,000 EGP
Journal entry	Accountant prepares the draft	Finance Manager posts and sets the lock date	—
Stock count	Keeper counts the location	Warehouse Manager applies the adjustment	—
POS refund	Cashier sells	Showroom Supervisor refunds	—

ALSO CONTROLLED

- ✓ Sales reps see only their own documents
- ✓ Chart of accounts, price lists and lock dates limited to named roles
- ✓ Chatter records who changed what
- ✓ Employee data handled under Law No. 151 of 2020
- ✓ Joiner, mover and leaver procedure with quarterly review

PART 05 / 05

Testing, training and go-live

05

Proving the system works, teaching the people, and switching over on the first day of the fiscal year.

- ✓ UAT & training
- ↶ Cutover & rollback
- $ Investment

SECTION · DIVIDER

GO-LIVE · CUTOVER PLAN

From UAT to go-live

Two test cycles, ten training sessions and a cutover with a validation pack and a rollback plan.

25	70	10	36	14	4
UAT SCENARIOS	REQUIREMENTS COVER	TRAINING SESSIONS	HOURS OF MATERIAL	VALIDATION CHECKS	WEEKS HYPERCARE

28–29 Dec

Master data frozen

Master data frozen and imported into production; every key user verifies their own data.

30–31 Dec

Stock count

Full stock count in all five warehouses and the showroom; legacy system closed for posting.

1 Jan

Go-live

Opening stock and opening entry posted, validation pack run, go / no-go meeting with the sponsor.

3 Jan

First working day

First POS session, first delivery and first invoice with a consultant watching.

⚠ If something goes wrong

- Backup before every import step
- Files re-importable by external ID
- Opening entry can be reset and reposted
- Legacy kept read-only for history


COMMERCIAL · YEAR 1

The investment

142 consultant days plus the Odoo subscription — payment released against seven signed milestones.

Year 1 cost breakdown

EGP · VAT EXCL.

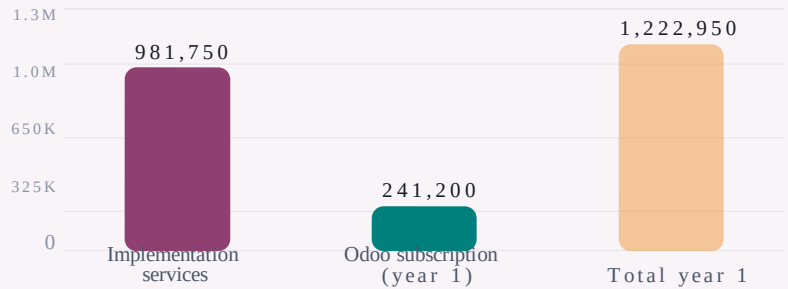

Figures are project assumptions; the cost model recalculates from the day rate and user count. VAT excluded.

What drives the price

- 142 days across 8 phases, including 15 days of customization
- 30 users on the Odoo Custom plan (Studio is required)
- 10% risk contingency, VAT excluded

Payment milestones

7 OF 7 SIGNED



kick-off	20%	BRD	15%
design	15%	build	20%
UAT	15%	go-live	10%
hypercare	5%		

142
CONSULTANT DAYS

7
SIGNED MILESTONES

What we learned

The decisions that made the biggest difference on this project.

01

Data before configuration

Building the 27 import files first exposed the real problems early: a chart of accounts with 17 duplicates, an inventory balance that did not match the products, and currencies locked on the wrong accounts.

DISCOVERY · 27 FILES · 17 DUPLICATES FOUND

02

Standard first

Every requirement was tested against standard Odoo before anyone opened Studio, which is why only 16% needed customization.

GAP ANALYSIS · STUDIO RESERVED FOR THE 16%

03

One owner per module

Each of us owned a module end to end — design, configuration, testing and the user guide — so nothing fell between people.

ACCOUNTABILITY · SINGLE OWNER, END TO END

04

Traceability

A pain point becomes a requirement, a requirement becomes a design section and a test case; at any moment we can show why a setting exists.

PAIN → REQUIREMENT → DESIGN → TEST

• KHOMASI ERP · LIVE DEMO NEXT

Thank you.

Live demo: lead→quotation→import with landed costs→fan assembly→showroom sale→financial statements.

70	89	27	1 Jan 2027
REQUIREMENTS	PRODUCTS	IMPORT FILES	GO-LIVE

▣ REPOSITORY

4 folders · 10 project documents · 3 entity-data workbooks · 27 import files

◎ TEAM

Ahmed Fahmy · Lobna Zanaty · Mayada Salah · Noha Gamal · Omar ElSayed

Khomasi ERP · Smart Core · DEPI Graduation Project · Beitak Smart · Odoo 19 Enterprise
